NUWAKOT DISTRICT PROGRESS STATUS - PHASE 1

% Complete	Task Name	Baseline Start	Baseline Finish	Actual Start	Actual Finish
100%	**Govt. of India Funded Reconstruction of 70 School Building & 1 Library in Earthquake affected Districts of Nepal.**	**Fri 11/30/18**	**Mon 11/9/20**	**Fri 11/30/18**	**Mon 11/9/20**
100%	**Nuwakot-Disctrict**	**Fri 11/30/18**	**Mon 11/9/20**	**Fri 11/30/18**	**Mon 11/9/20**
100%	School ID-43 (17(3S-9C),10(2S-4C), 20(TCM))	Mon 12/17/18	Mon 11/9/20	Mon 12/17/18	Mon 11/9/20
100%	School ID-44 (16(2S-6C), 22(2AC), 20(TCM))	Sun 12/16/18	Mon 10/12/20	Sun 12/16/18	Mon 10/12/20
100%	School ID-45 (16(2S-6C), 18(2-LaLiEM), 22(2AC), 20(TCM))	Mon 12/17/18	Thu 3/12/20	Mon 12/17/18	Thu 3/12/20
100%	School ID-46 (17(3S-9C), 106(2S-6C), 20(TCM))	Sun 12/16/18	Mon 2/10/20	Sun 12/16/18	Mon 2/10/20
100%	School ID-50 (10(2S-4C),18(2-LaLiEM), 16(2S-6C), 22(2AC), 20(TCM))	Fri 11/30/18	Wed 7/8/20	Fri 11/30/18	Wed 7/8/20

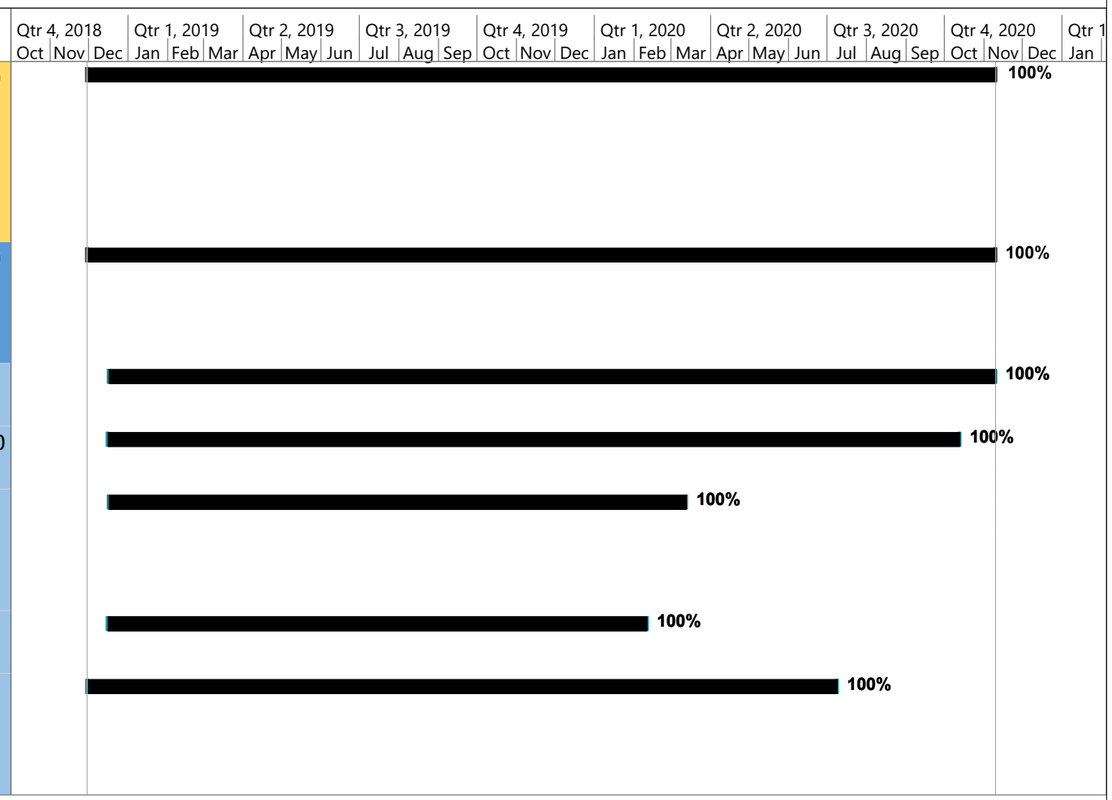

Project: Govt. of India Funded Recons
Date: Mon 8/16/21

Task		Inactive Task		Manual Summary		Deadline		Manual Progress	
Split		Inactive Milestone		Start-only		Baseline		Summary	
Milestone		Inactive Summary		Finish-only		Baseline Milestone		Completed	
Summary		Manual Task		External Tasks		Baseline Summary			
Project Summary		Duration-only		External Milestone		Progress			
