# LALITPUR DISTRICT PROGRESS STATUS

| % Complete | Task Name | Baseline Start | Baseline Finish | Actual Start | Actual Finish | Cost |
|---|---|---|---|---|---|---|
| **100%** | **Lalitpur District** | **Fri 6/25/21** | **Sat 3/25/23** | **Fri 6/25/21** | **Sat 3/25/23** | **Rs. 0.00** |
| **100%** | **Package 1** | **Fri 6/25/21** | **Sat 3/25/23** | **Fri 6/25/21** | **Sat 3/25/23** | **Rs. 0.00** |
| **100%** | **Health Post ID-146, Bisankhu Narayan Ayurbed Aausadhalaya (AA)** | **Fri 6/25/21** | **Sat 3/25/23** | **Fri 6/25/21** | **Sat 3/25/23** | **Rs. 0.00** |

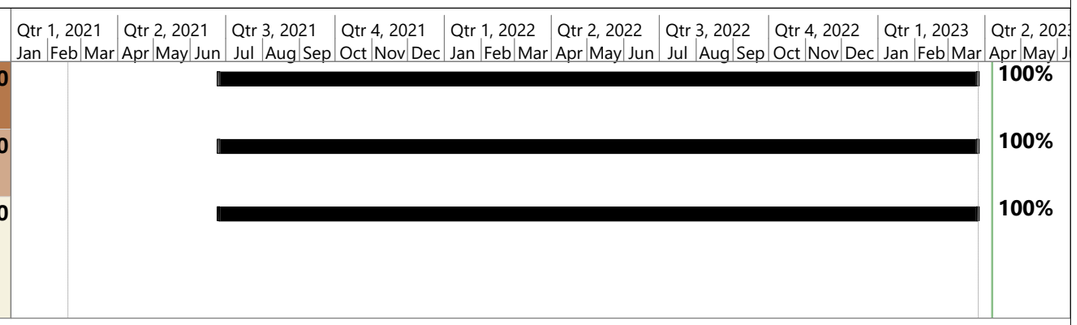


Project: TYPE4
Date: Fri 4/7/23

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Progress | Manual Progress
