KAVRE DISTRICT PROGRESS STATUS - PHASE 3

% Complete	Task Name	Baseline Start	Baseline Finish	Actual Start	Actual Finish	PMC ENGINEER
40%	**Kavre-District**	Tue 2/9/21	Thu 5/5/22	Tue 2/9/21	NA	
31%	School ID-75 (24(3S-13C))	Tue 2/9/21	Thu 5/5/22	Tue 2/9/21	NA	Birendra Karki
54%	School ID-76 (17(3S-9C) & 19(TCS))	Tue 2/9/21	Thu 5/5/22	Tue 2/9/21	NA	Birendra Karki

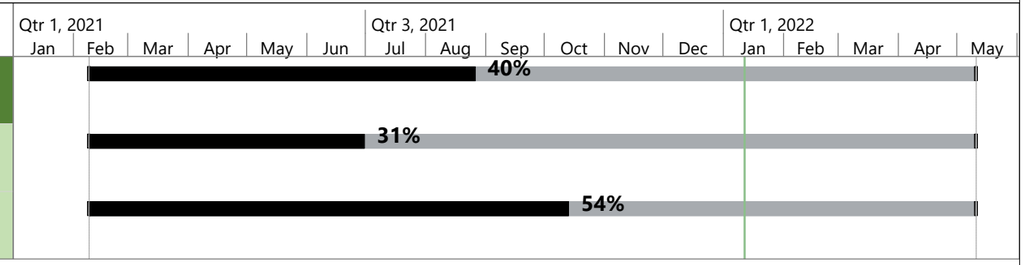

Project: Master Schedule_R0_Ju
Date: Wed 1/12/22

Task	Project Summary	Manual Task	Start-only	Deadline
Split	Inactive Task	Duration-only	Finish-only	Progress
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress
Summary	Inactive Summary	Manual Summary	External Milestone	Completed
