GORKHA DISTRICT PROGRESS STATUS - PHASE 1

% Complete	Task Name	Baseline Start	Baseline Finish	Actual Start	Actual Finish
100%	**Govt. of India Funded Reconstruction of 70 School Building & 1 Library in Earthquake affected Districts of Nepal.**	**Sun 12/2/18**	**Fri 11/27/20**	**Sun 12/2/18**	**Fri 11/27/20**
100%	**Gorkha-Disctrict**	**Sun 12/2/18**	**Fri 11/27/20**	**Sun 12/2/18**	**Fri 11/27/20**
100%	School ID-63 (17(3S-9C(1)), 18(2-LaLiEM))	Sun 12/2/18	Fri 11/27/20	Sun 12/2/18	Fri 11/27/20
100%	School ID-65(17(3S-9C), 18(2-LaLiEM), 10(2S-4C), 20(TCM))	Sun 12/2/18	Fri 11/27/20	Sun 12/2/18	Fri 11/27/20
100%	School ID-66 (17(3S-9C), 10(2S-4C), 20(TCM))	Sun 12/16/18	Fri 11/27/20	Sun 12/16/18	Fri 11/27/20

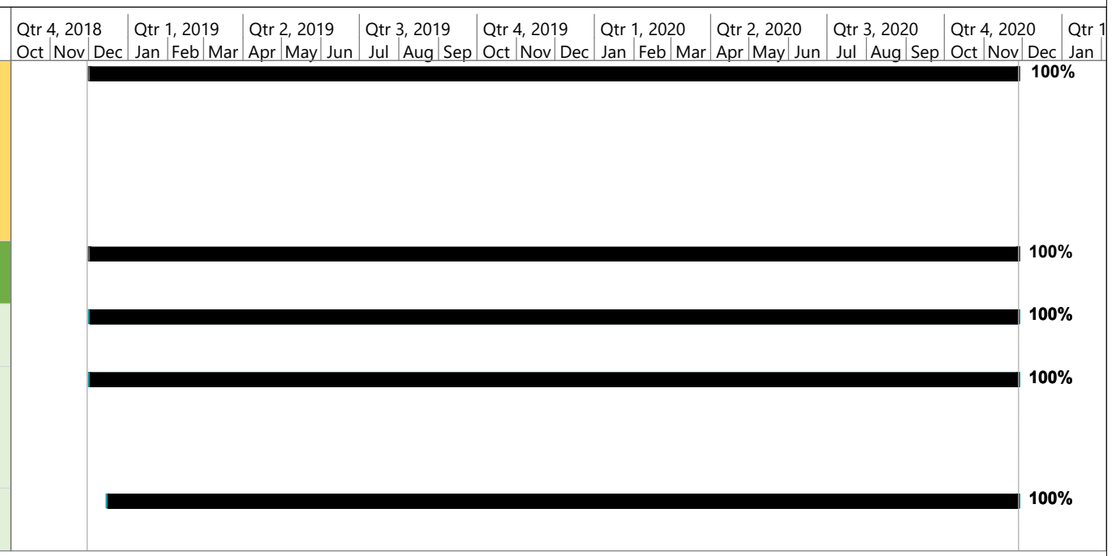

Project: Govt. of India Funded Recons
Date: Mon 8/16/21

Task		Inactive Task		Manual Summary		Deadline		Manual Progress	
Split		Inactive Milestone		Start-only		Baseline		Summary	
Milestone		Inactive Summary		Finish-only		Baseline Milestone		Completed	
Summary		Manual Task		External Tasks		Baseline Summary			
Project Summary		Duration-only		External Milestone		Progress			
