KAVRE DISTRICT PROGRESS STATUS - PHASE 3

% Complete	Task Name	Baseline Start	Baseline Finish	Actual Start	Actual Finish	PMC Engineer
100%	**Kavre-District**	**Tue 2/9/21**	**Mon 5/15/23**	**Tue 2/9/21**	**Mon 5/15/23**	
100%	**School ID-75 (24(3S-13C))**	**Tue 2/9/21**	**Mon 5/15/23**	**Tue 2/9/21**	**Mon 5/15/23**	**Indrajit Yadav**
100%	**School ID-76 (17(3S-9C) & 19(TCS))**	**Tue 2/9/21**	**Fri 3/31/23**	**Tue 2/9/21**	**Fri 3/31/23**	**Indrajit Yadav**

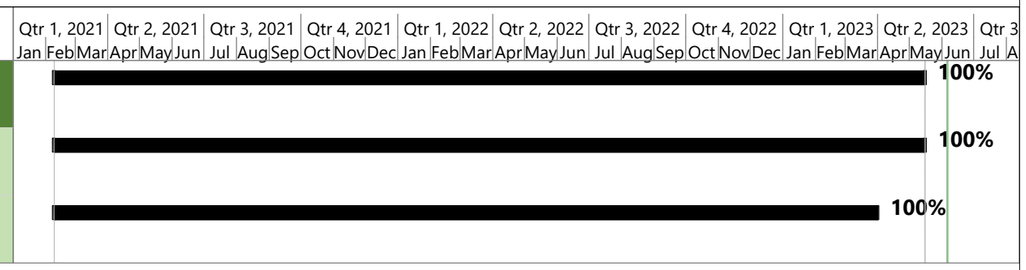

Project: Master Schedule_R0_Ju
Date: Tue 6/6/23

Task	Project Summary	Manual Task	Finish-only	Progress
Split	Inactive Task	Duration-only	External Tasks	Manual Progress
Milestone	Inactive Milestone	Manual Summary	External Milestone	Completed
Summary	Inactive Summary	Start-only	Deadline	
